

Active Projects Dashboard


Last Update:

10/02/20


Projects Report Summary

Status	Primary	Upcoming Milestone Date	Update
In Progress - On Track	Airport Master Plan Updates	09/30/20	Kickoff meeting complete prior to Milestone Date
In Progress - On Track	East Apron Rehab - Design Phase	TBD	Project has begun with Hoyle Tanner
In Progress - On Track	Master Drainage Plan	09/30/20	Kickoff meeting complete prior to Milestone Date
In Progress - On Track	Wildlife Hazard Assessment	07/15/21	Wildlife expert provides monthly updates, Milestone Date is estimated completion
In Progress - On Track	Crystal Lake Park Connector Trail	10/16/20	Integrating feedback from the Public Open House into the 30% Design Concept
In Progress - On Track	Mimi Hardman Collections & Research	09/30/20	
In Progress - On Track	NW Sidewalk Program	10/09/20	Milestone Date: City to receive draft report
In Progress - On Track	Park Avenue Streetscape	10/30/20	Tentative 60% Construction Drawings Review
In Progress - On Track	Recreation Master Plan	10/30/20	Staff currently awaiting agreement proposal from S&ME
In Progress - On Track	Sports Feasibility Analysis Study	10/16/20	Draft analysis is expected in mid-October from consultant
In Progress - On Track	YMCA Implementation Phase 2	10/30/20	Staff is in the process of finalizing improvement plan to take place this FY
Behind	Hwy 27 & Hwy 60 Interchange Project	10/30/20	Area 1: Henry Street & Hwy 60 - W & FM work underway FDOT progress teleconference next Progress Meeting 8/4/20 Directional Bores to start next week 1st-Central, 2nd-Hwy60/Crazy Fish, 3rd-Miami/Hwy 60, 4th-Hwy 27 south 4th and final bore TBC All bores are complete. Fields Caddallic and Central Avenue tie-in complete The tie-ins are underway with completion set for the week of 8/31/20 The project is behind considering the completion date, but Freddie is coordinating with DOT and we are staying ahead of their contractor so it is not a problem new completion estimated for 10/30/20
Complete	HS GST WTP#3	10/16/20	Finalizing as-built for partial clearance substantial completion extended to August 28th Substantial completion walk-thru finalizing clearance packet and closing out the punch list Project is complete w/ one punch list item remaining - schedule for completion 9/2/20 Final two pay applications are under review This project is complete with the exception of two sleeves that are on back order. This is the last item remaining and retainage can be released. The contractor reported that the sleeves have been delayed but anticipate them arriving next week
In Progress - On Track	Western Expansion Phase II	10/14/20	Commission Approved HMB contract Phase II gearing up Pre-con 6/25/2020 Start date TBD HMB has started staging pipe in the ROW for boring Forcemain boring under way Watermain boring set for 8/17/20 next progress meeting 10/14/20; project is on tract and there have not been any delays

Airport Specific

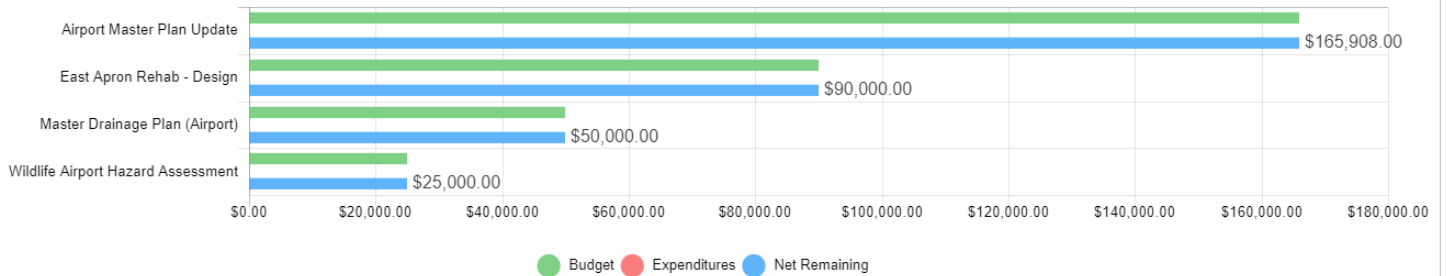

General Projects

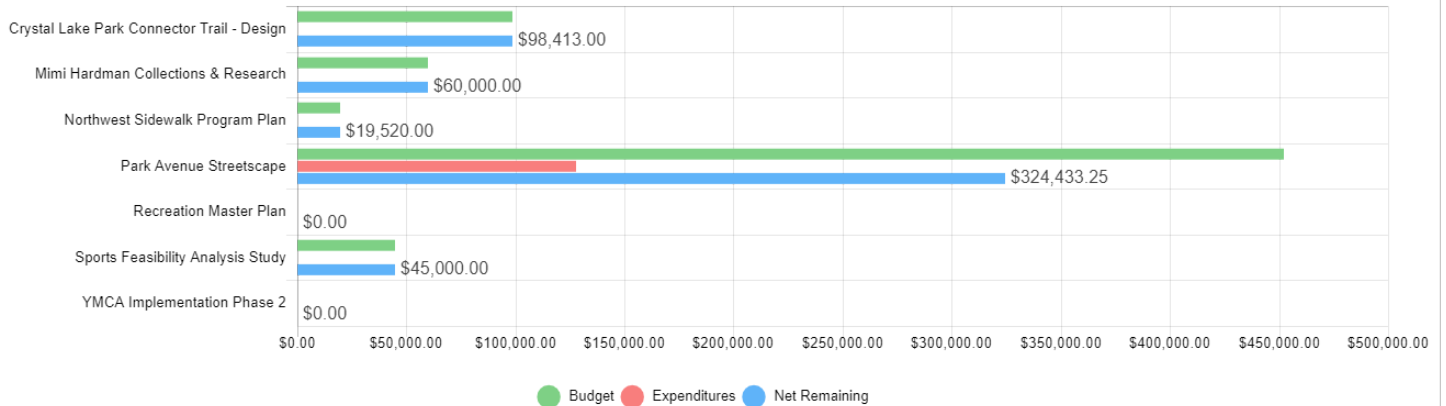

Utilities Specific

